




KPI PERFORMANCE DASHBOARD









Period : Feb 2024 – Oct 2025



KPI OVERVIEW

TOTAL PROJECTS 100 Across Portfolio	TOTAL TASKS 300 work items tracked	Completed Task 87 29% Task Completed	Completed Project 26 26% Project Completed	OVER-BUDGET TASKS 7 cost-control watchlist	TASK COMPLETION % 29.0% tasks fully complete
EARNED VALUE \$1,085,090 value of work performed	AVG PROGRESS 63.6% mean task completion	AVG DURATION \$148 planned task length	HOURS LOGGED 5,763 Total Effort	TASKS BILLED 93 of 300 have actuals	PORTFOLIO CPI 0.290 earned value / actual
TOTAL BUDGET \$1,687,280 allocated funds	BUDGET UTILIZATION 30.7% spend vs budget	ACTUAL SPEND \$518,421 committed to date	BUDGET AT RISK \$16,457 overrun across 7 tasks	ON-BUDGET RATE 92.5% billed tasks within budget	COST VARIANCE \$5,084 favorable vs budget

PERFORMANCE OVERVIEW

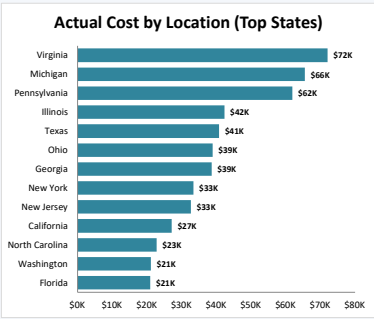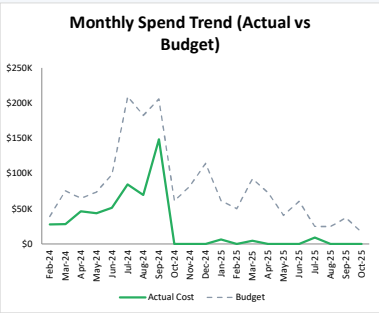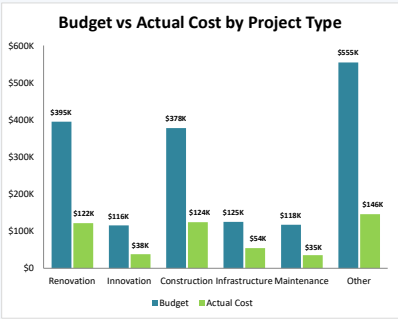





Status x Priority - Task Heatmap

	High	Medium	Low
Behind	45	27	15
On Track	44	19	12
On Hold	30	17	13
Completed	37	28	13

Cell = task count; deeper red = higher concentration

Project	Task	Project Name	Owner	Type	Budget	Actual	Overrun \$	% Over
P075	T001	Building a Park Project 075	Ivy	Other	\$8,493	\$12,398	\$3,905	46%
P010	T001	Airport Expansion Project 010	Grace	Other	\$1,577	\$4,850	\$3,273	208%
P096	T002	Office Building Renovation 096	Frank	Renovation	\$2,984	\$6,060	\$3,076	103%
P027	T002	University Dormitory Constr. 027	Bob	Construction	\$1,646	\$4,190	\$2,544	155%
P094	T003	Road Expansion Project 094	Charlie	Infrastructure	\$1,447	\$3,357	\$1,910	132%
P052	T001	Apartment Complex Dev. 052	Ivy	Other	\$8,114	\$9,104	\$990	12%
P022	T003	Apartment Complex Dev. 022	Ivy	Other	\$1,424	\$2,183	\$759	53%

KEY INSIGHTS

- Spend is heavily back-loaded: only **30.7%** of the **\$1.69M** budget is committed to date, signalling an early-stage or schedule-delayed portfolio.
- Delivery risk is concentrated: **49 of 100** projects are Behind or On Hold, versus **26 Completed** — nearly half the portfolio needs intervention.
 - September 2024 is the spend peak at **\$148K** (**29%** of all actual cost), worth investigating for cost spikes or milestone clustering.
- Workload is concentrated: Charlie and Alice carry **114 of 300 tasks** (38%) and **~40%** of logged hours — a key-person dependency risk.
- Cost control: **7 tasks** are over budget by a combined **\$16.5K**; High-priority items make up **52%** of tasks, suggesting priority inflation.
- Overruns cluster in "Other" projects (4 of 7), led by Park P075 (+46%) and Airport P010 (+208%) - both warrant scope/estimate root-cause reviews before more cash is committed.
 - Risk quadrant: "Other" (\$555K) and "Renovation" (\$395K) pair the largest budgets with the lowest average progress (~60-62%) - highest exposure, slowest burn.
- Resourcing is capacity-bound, not skill-bound: Frank leads on completion rate (44%) with the lightest load, while the two heaviest workloads (Charlie, Alice) sit near the portfolio-low ~26% - rebalancing should lift throughput.
- Schedule: average planned task duration is 148 days; Innovation runs longest (237 days), compounding its delivery risk and tying up budget for longer.
- Budget is geographically diversified - it takes ~10 of 13 states to reach 80% of spend - limiting single-location dependency but offering little vendor-consolidation leverage.

